



Quad City P-25 Radio Project

UPDATE
AUGUST 2021

Project Summary – Contracts (SC only)

- **Tower Sites:** T. Steele Construction from Milan, IL for \$1.98 M; includes towers, compounds, utilities and fixed equipment
- **Radio System:** Racom Corp from Marshalltown, IA for \$8.66 M for the radio system, devices, dispatch equipment and project management
- **Project Consulting and Tower Engineering:** True North Consulting Group from Stillwater, MN with a sub-contract with Edge Consulting Engineers from Prairie Du Sac, WI for a total amount of \$604,000
- **Logging Recorder:** Nelson Systems, from Springfield, IL for \$120,000
- **Total Project Cost:** \$13 M

Project Summary – Tower Project

- **Tower Sites:** construction complete pending punch list items;
- **Tower Site Equipment:**
 - Antennas and lines installed all sites except SECC
 - Racks of transmitting (RF) and microwave equipment installed
- **System Start-up:**
 - Expecting various components to start-up during August into early Sept
 - Testing to begin during September

Project Summary – Radio Devices

- All radio devices ordered and with Racom
- Portable Radios delivered to several agencies
- Order of delivery is determined/tentative schedule
- Finalizing layout of talk groups for each agency
- Project schedule calls for all radios delivered and switched over to new system by EOY
- Issue with mobile radios for Law Enforcement

Project Summary – Other Work

- **Symphony Consoles** (radio computers) installed at all locations
- **New Recorder** is installed and recording old system and new components as they come on-line. One issue with phone vendor to resolve.
- **Phoenix System** is installed and training underway. There are some issues remaining with Fire Agencies and workflows, but we are working to resolve.
- **Decommissioning** is underway with radio devices. We are working to determine salvage value, if any.

Bettendorf



Bettendorf

Sabre Industries™
Towers and Poles

MODEL / JOB#: 468795

TOWER HEIGHT: 260 FT. S3TL-HD1

LOCATION: BETTENDORF, IA

468795



Bettendorf



Walcott




Walcott



Walcott



Buffalo

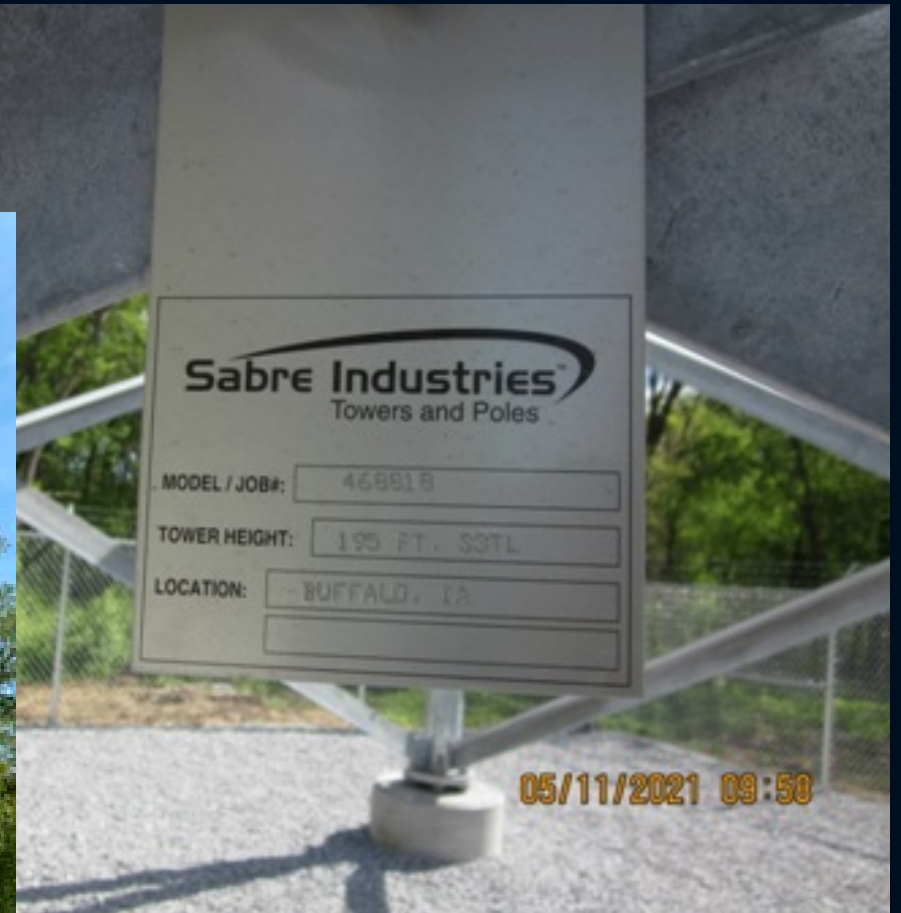

Buffalo



Buffalo



Buffalo



THERMO BOND BUILDINGS
Elk Point, SD 57025 * Elkhart, IN 46517 * 800-356-2686



Scott County, IA


Serial #: 2007-389A-4 **Size:** 12'x16'x9'
Model #: TBB 1261 **Site:** Buffalo




Scott County Park



Scott County Park

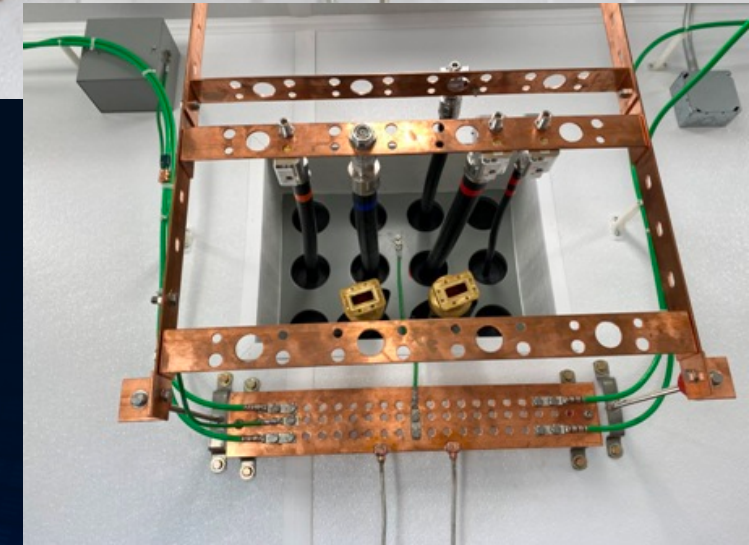

Scott County Park

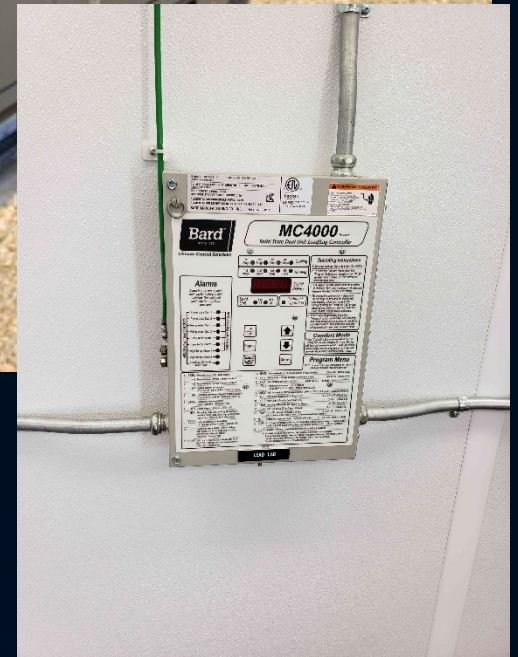

South Utah



South Utah



Princeton



Princeton



SECC



Quad City P-25 Radio Project

UPDATE
AUGUST 2021

QUESTIONS?
